










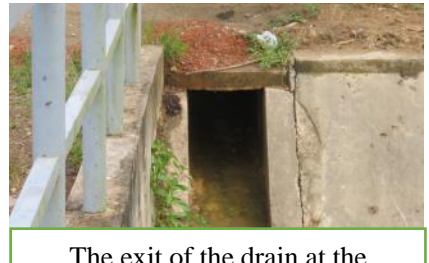


**Bi weekly Field Report**











**No. 69**







Surveyor Zaw La  
 Date visited 20 Sep 2019  
 Time visited 10:15 am

Weather Condition Cloudy  
 The last time of heavy raining: Yesterday

No	Item	Condition	Narrative Description and Photos
1	(1.1) Water Supply System	Improved <input type="checkbox"/> Same <input checked="" type="checkbox"/> * Worse <input type="checkbox"/> *as last week	<p><b><u>Narrative Description</u></b></p> <p>Water distribution system has been supporting ninety household of the zone B resettled families. The new well was drilled and installed the pipe line and its necessary instruments because the underground water of the previous well includes iron hydroxide and yellowish mud that clogged in the iron removal tank. The current water condition is quite good and no iron hydroxide and yellowish mud are found.</p> <p><b><u>Photos</u></b></p> <div style="display: flex; flex-wrap: wrap;"> <div style="width: 50%; text-align: center;">  </div> <div style="width: 50%; text-align: center;">  </div> <div style="width: 50%; text-align: center;">  <p>Water from ground water tank</p> </div> <div style="width: 50%; text-align: center;">  <p>Pipe line distribution water to houses</p> </div> <div style="width: 50%; text-align: center;">  </div> <div style="width: 50%; text-align: center;">  </div> </div>

No	Item	Condition	Narrative Description and Photos
1	(1.2) Well	Improved <input type="checkbox"/> Same <input checked="" type="checkbox"/> * Worse <input type="checkbox"/> <i>*as last week</i>	<p>– Water from two open-wells is clean enough to use for drinking and living. There are eleven tube wells in the relocation site. Residents use the water basically from the pipeline distribution system so that the frequency of water usage from the tube wells is very low. To sustain the good condition of the tube wells, the leg pumps were kept and covered the PVC pipes with the caps till the residents use.</p>
			<div style="display: flex; justify-content: space-around;"> <div style="text-align: center;">  <p>Open Well No. 1</p> </div> <div style="text-align: center;">  <p>Open Well No. 2</p> </div> </div>
	(2) Drainage	Improved <input type="checkbox"/> Same <input checked="" type="checkbox"/> * Worse <input type="checkbox"/> <i>*as last week</i>	<p>– There is a little amount of water in the drainage canals at the moment.</p> <p><b>Photos</b></p> <div style="display: grid; grid-template-columns: 1fr 1fr; gap: 10px;"> <div style="text-align: center;">  <p>The drain at the corner of Main Road A and B</p> </div> <div style="text-align: center;">  <p>The exit of the drain at the corner of Site village road and 2<sup>nd</sup> street</p> </div> <div style="text-align: center;">  <p>The exit of the drain at the corner of Site village road and 3<sup>rd</sup> street</p> </div> <div style="text-align: center;">  <p>The exit of the drain at the corner of Site village road and Main Road C</p> </div> </div>
	(3) Road	Improved <input type="checkbox"/> Same <input checked="" type="checkbox"/> * Worse <input type="checkbox"/> <i>*as last week</i>	<p>– All the roads except 6<sup>th</sup> street are still dry and no problem for walking. 6<sup>th</sup> street is being damaged due to passing the heavy trucks that carry the soil to fill near the creek side. Therefore the exits of the drain at the 6<sup>th</sup> street are being blocked with the soil.</p> <p><b>Photos</b></p>

		 <p>Main Road - B</p>	 <p>1<sup>st</sup> Street</p>
		 <p>2<sup>nd</sup> Street Upper Block</p>	 <p>2<sup>nd</sup> Street Lower Block</p>
		 <p>3<sup>rd</sup> Street Upper Block</p>	 <p>3<sup>rd</sup> Street Lower Block</p>
		 <p>4<sup>th</sup> Street Upper Block</p>	 <p>4<sup>th</sup> Street Lower Block</p>
		 <p>5<sup>th</sup> Street</p>	 <p>6<sup>th</sup> Street</p>

			 <p>7<sup>th</sup> Street</p>	 <p>Site Village</p>
(4) Garbage Condition	Improved <input type="checkbox"/> Same <input checked="" type="checkbox"/> * Worse <input type="checkbox"/> <i>*as last week</i>	<ul style="list-style-type: none"> <li>- The rubbish was dumped at the creek side and even in front of the houses before the enough garbage bins are provided.</li> <li>- Total fourteen garbage bins have been provided and placed at the corner of each road until the end of April. After April 2018, all the garbage bins are kept by the community leader of PAPs in the communal compound near the triangle junction of Main Road C and Upper Fourth Street. But starting from October, the garbage truck from township municipal office came and collected by giving its alarm along the Main Road B.</li> </ul> <p><b>Photos</b></p>		
			 <p>Rubbishes in the creek near 1st street</p>	 <p>Rubbishes in the creek near 2nd street</p>
			 <p>The soil was filled near the creek of Main Road C in March</p>	 <p>The soil was filled near the creek of 6<sup>th</sup> Street in March</p>

(5) Fly proof toilet

Improved   
 Same \*  
 Worse   
 \*as last week

- All of the fly proof toilets are used the residents.
- All of the toilets are repaired by the following procedures;
  - Installation the extra septic tanks beside the original
  - The pipe line system is installed from the extra tank to the ditch to flow the liquid out.

The toilet renovation plan was successfully done and there is no problem at the moment.

Condition	No. of HHs	
	This week condition	Previous week condition
Level 1	91	91
Level 2	0	0
Level 3	0	0
Level 4	0	0
No Toilet	0	0

**<Evaluation Criteria>**

**Level 1**

- Fly proof toilet is not needed to be repaired.
- No/rarely toilet unavailable

**Level 2**

- Fly proof toilet is needed to be repaired.
- Rarely toilet unavailable

**Level 3**





- Fly proof toilet is needed to be repaired.
- Often toilet unavailable
- As the result of filling the soil and also due to the heavy rain, some toilets are inconvenience to use.


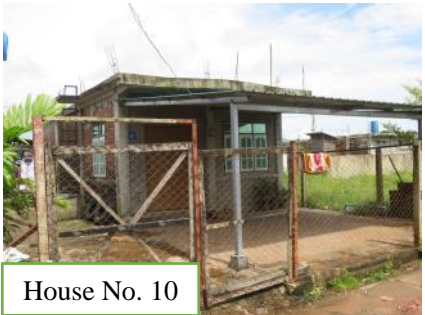

**Level 4**







- Fly proof toilet is urgently needed to be repaired.
- Often toilet unavailable

**Photos**



	(6) Electricity	Improved <input type="checkbox"/> Same <input checked="" type="checkbox"/> * Worse <input type="checkbox"/> <i>*as last week</i>	<ul style="list-style-type: none"> <li>– Residents get the electricity regularly.</li> <li>– Electric poles and transformer are being supported with the good foundations.</li> <li>– There are some pieces of wood under an electric pole of main road B and it's needed to clean up.</li> </ul> <p><b>Photos</b></p> <div style="display: flex; flex-wrap: wrap;"> <div style="width: 50%; text-align: center;">  <p>Transformer No. 1</p> </div> <div style="width: 50%; text-align: center;">  <p>Transformer No. 2</p> </div> <div style="width: 50%; text-align: center;">  <p>Transformer No. 3</p> </div> <div style="width: 50%; text-align: center;">  <p>Electric poles of Main Road B and Main Road C</p> </div> </div>
--	--------------------	---	---

No	Item	Condition	Description and Photos
2	(1)House Construction	No. of houses which are not completed (4)	<ul style="list-style-type: none"> <li>– In plot No.9 and 10, three houses that are planned to build as the plots are owned by father and son. The second floors of these three houses are needed to be carried on.</li> <li>– Plot No. 66, the house construction for the first floor has been finished and the second floor is still needed to be carried on.</li> </ul> <p><b>Photos</b></p> <div style="display: flex; flex-wrap: wrap;"> <div style="width: 50%; text-align: center;">  <p>House No. 9</p> </div> <div style="width: 50%; text-align: center;">  <p>House No. 10</p> </div> <div style="width: 50%; text-align: center;">  <p>House No. 66</p> </div> </div>

3	Other Issues	<p data-bbox="568 129 702 161"><u>Description</u></p> <table border="1" data-bbox="568 192 1155 430"> <thead> <tr> <th data-bbox="568 192 753 295" rowspan="2">Condition</th> <th colspan="2" data-bbox="759 192 1155 224">No. of HHs</th> </tr> <tr> <th data-bbox="759 232 938 295">This week condition</th> <th data-bbox="944 232 1155 295">Previous week condition</th> </tr> </thead> <tbody> <tr> <td data-bbox="568 304 753 331">Level 1</td> <td data-bbox="759 304 938 331">82</td> <td data-bbox="944 304 1155 331">82</td> </tr> <tr> <td data-bbox="568 340 753 367">Level 2</td> <td data-bbox="759 340 938 367">5</td> <td data-bbox="944 340 1155 367">5</td> </tr> <tr> <td data-bbox="568 376 753 403">Level 3</td> <td data-bbox="759 376 938 403">3</td> <td data-bbox="944 376 1155 403">3</td> </tr> <tr> <td data-bbox="568 412 753 439">Level 4</td> <td data-bbox="759 412 938 439">1</td> <td data-bbox="944 412 1155 439">1</td> </tr> </tbody> </table> <p data-bbox="568 465 845 497">&lt;Evaluation Criteria&gt;</p> <p data-bbox="568 501 654 533"><b>Level 1</b></p> <p data-bbox="568 537 1372 591">-No mud and no standing water with their own drainage system in their compound</p> <p data-bbox="568 595 654 627"><b>Level 2</b></p> <p data-bbox="568 631 1139 663">-No mud and no standing water in their compound</p> <p data-bbox="568 667 660 698"><b>Level 3</b></p> <p data-bbox="568 703 1228 734">- Some or little mud and standing water in their compound</p> <p data-bbox="568 739 654 770"><b>Level 4</b></p> <p data-bbox="568 775 1155 806">-A lot of mud and standing water in their compound</p> <p data-bbox="568 819 1410 918">Remark: The compound of house no. 47 will not be muddy again as it has been renovated with concrete. Therefore the other photo for level 3 will be changed in the next report.</p> <p data-bbox="568 949 654 981"><b>Photos</b></p> <div data-bbox="568 985 1002 1294"> <p data-bbox="574 994 708 1025">Level 1</p>  <p data-bbox="574 1258 778 1290">House No. 31</p> </div> <div data-bbox="1021 985 1452 1294"> <p data-bbox="1027 994 1161 1025">Level 2</p>  <p data-bbox="1027 1258 1232 1290">House No. 19</p> </div> <div data-bbox="568 1308 1002 1617"> <p data-bbox="574 1317 708 1348">Level 3</p>  <p data-bbox="574 1581 778 1612">House No. 64</p> </div> <div data-bbox="1021 1308 1452 1617"> <p data-bbox="1027 1317 1161 1348">Level 4</p>  <p data-bbox="1027 1581 1232 1612">House No. 84</p> </div> <div data-bbox="568 1653 1002 1962"> <p data-bbox="574 1662 708 1693">Level 3</p>  <p data-bbox="574 1926 778 1957">House No. 75</p> </div> <div data-bbox="1021 1653 1452 1962"> <p data-bbox="1027 1662 1161 1693">Level 4</p>  <p data-bbox="1027 1926 1232 1957">House No. 88</p> </div>	Condition	No. of HHs		This week condition	Previous week condition	Level 1	82	82	Level 2	5	5	Level 3	3	3	Level 4	1	1
Condition	No. of HHs																		
	This week condition	Previous week condition																	
Level 1	82	82																	
Level 2	5	5																	
Level 3	3	3																	
Level 4	1	1																	

(2) Plantation

- In front of the compounds, the shady trees, fruit trees, flowering plants and vegetables are being planted.

Description

- In front of the compounds, the shade trees, fruit trees, flowering plants and vegetables are being planted.

Type	No. of HHs	Remarks
Shade tree	15	Albizia, Indian almond, Neem tree, etc. HH No. 20, 40, 43, 48, 51, 57, 59, 61, 62, 67, 69, 72, 73, 77, 85
Fruit tree	37	Banana, Mango, sugar cane, coconut, citrus and jack fruit etc. HH No. 3, 15, 17, 20,21, 23, 28, 30, 31, 32, 34, 37, 40, 41, 48, 51, 52, 55, 57, 58, 59, 61, 62, 63, 67, 68, 70, 71, 72, 73, 77, 78, 82, 85, 86, 88
Vegetables	20	Chili, tomato, bitter gourd, Roselle, gourd, basils, eggplant etc. HH No. 12, 17, 21, 41, 49, 58, 59, 61, 62, 63, 67, 68, 70, 71, 72, 73, 77, 82, 85, 86
Flowering plant	31	Jasmine, poinsettia, orchid, kiss me quick, etc. HH No. 3, 5, 6, 8, 10, 12, 13, 14, 17, 20, 21, 22, 23, 29, 30, 31, 32, 46, 48, 58, 59, 61, 62, 65, 67, 68, 69, 72, 77, 78, 86

**Photos,**



(3) Livestock

Description

- The chicken, geoses and ducks are being raised.

Type	No. of HHs	Remarks
Chicken	6	HH No. 13, 14, 21, 59, 67, 78
Duck	3	HH No.12
Goose	2	HH No. 40, 67



**Photos**



House No. 67



House No. 78
